BRHAT BANGALORE MAHANAGARA PALIKE

INSPECTION REPORT

Sl No	Decription	Details	Remarks
1	Name of Work	Improvements to Roads and Drains at Ramanjenaya Layout Palanahalli in Ward No.05 Byatarayanapura Sub Division	
2	Estimate Cost	20.00 Lakhs	
3	Administrative Approved No and Date	602/13-14, Date. 23.12.2013	
4	Technical sanction No. and Date	45/13-14, Date. 23.012.2013	
5	Job Code No. and P Code No.	005-14-000017	
6	Tender Direct Entrested to KRIDL	Nil	
7	if Tender, Tender Notification No. Date and Publication in daily news Paper	/06.12.2013	
8	Tender Approved Details		
9	Work Order No and Date	72/2014-15, Date. 12.08.2014 Modified W.O . 86/14-15, Date. 27.08.2014	
10	Stipulation time of Completion	60 Days	
11	Actiual Date of Commencement	14.08.2014	
12	Actiual Date of Completion	30.08.2014	
13	Delay if any	Nil	

14	Reson for Delay	Nil	
15	Payment made till date.	Nil	
16	Status of Work	Completed	
17	Photograph verfied	Enclosed	
18	Date of Inspection	26.05.2015	
19	MB No. and Page No.	Mb No.2507 Page No. 250619-36	
20	BR No. and Date	295/30.08.2014	
21	Test Result	Quality Test Report submitted by Civil Tech Consultents and Engineers is verified and Enclosed	
22	Section officer	Sri P A Chandrakanthraju A.E	
23	Sub Division Office	Sri Shivakumar Goudar AEE Byatarayanaprua Sub Division	
24	Observation		
a	Work Quality	Satisfactory	
b	Comments	Work completed as per MB	

26/5/15

(Y. C. Kale Gowda)

Executive Engineer

(Retd)

Improvements to Roads & drain at Ramakrishnya Layout-
Balavanalli Ward No-5 Byatarayanna Sub-division

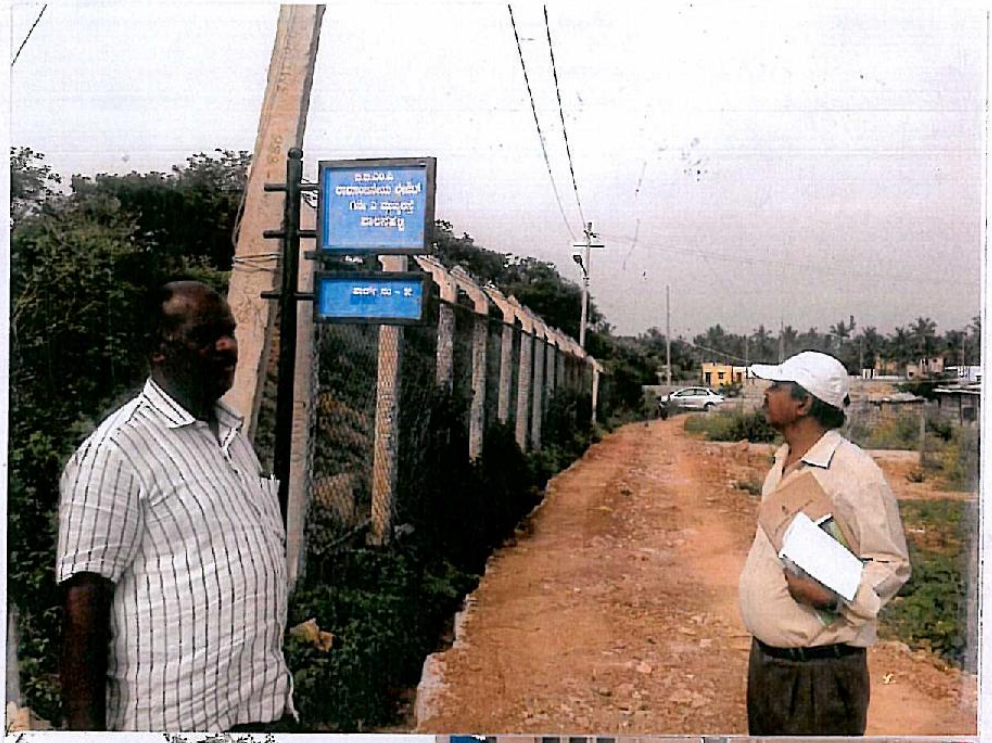

AE-05

Implemented to Roads & Drains at Ramanjenaya layout Palavahalli in ward no: 05.

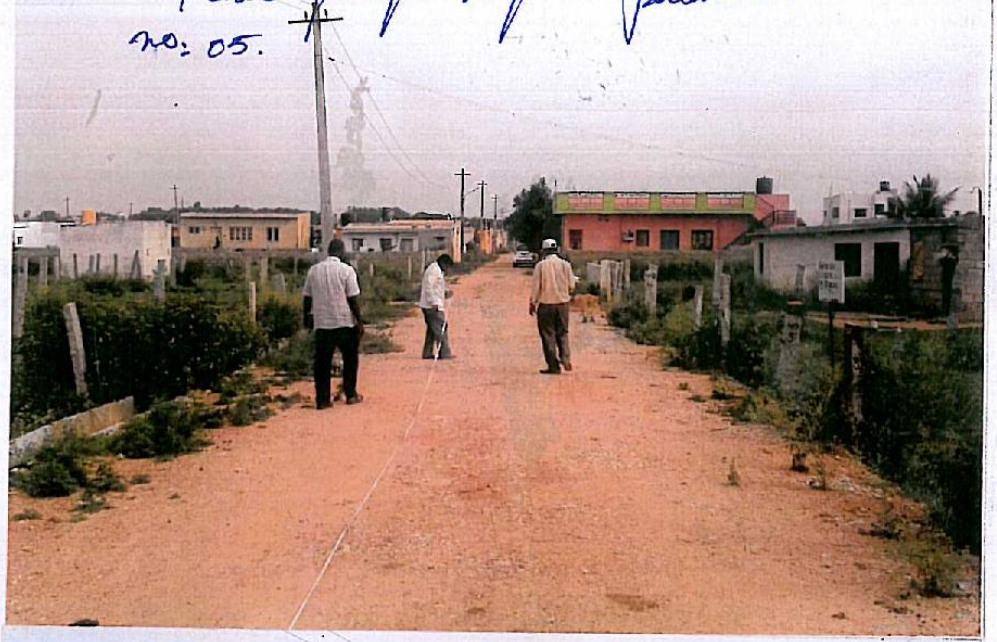

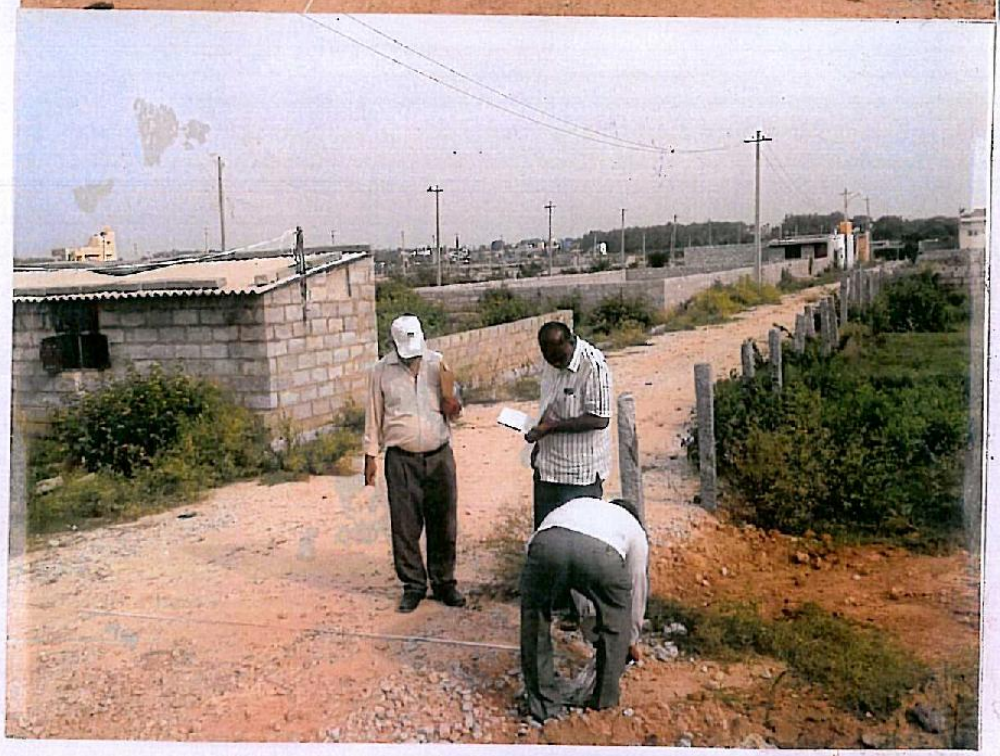

AE-05

Employment to Road & Drain at Ramanjanaya Layout palanahalli in ward no: 05

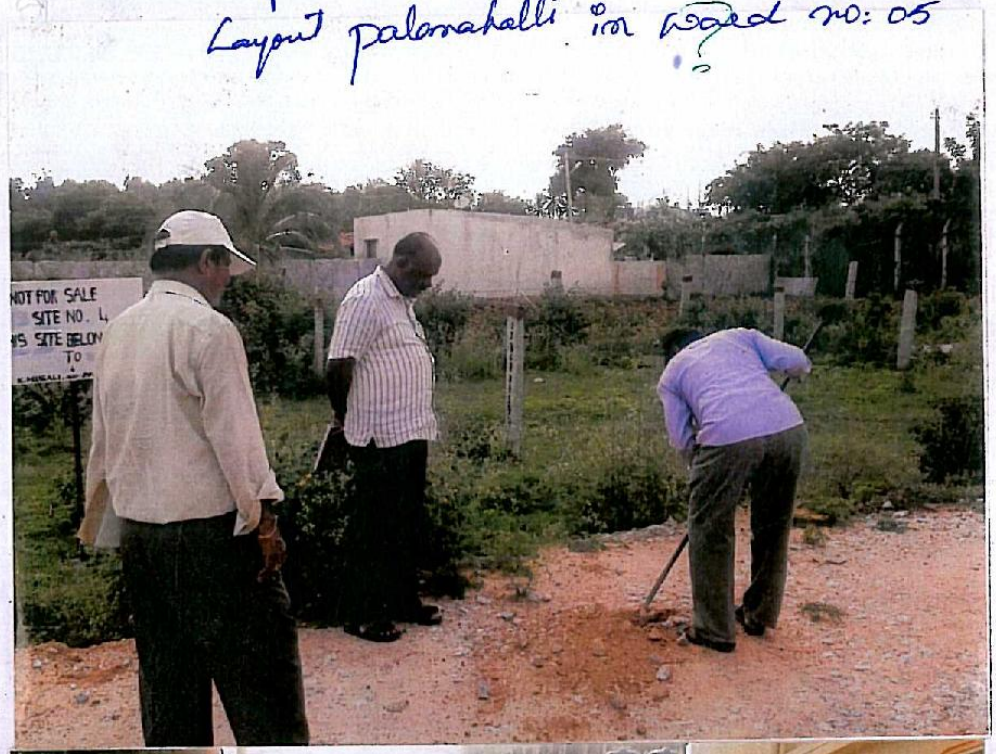

AE-05
